

## Fixed Scaffolding Erection and Dismantling | SAFE WORK METHOD STATEMENT (SWMS)

### TASK OR ACTIVITY: Fixed Scaffolding Erection and Dismantling

Business Name:	ABN:	SWMS#
Business Address:		
Contact Person:	Phone:	Email:

### THIS SAFE WORK METHOD STATEMENT IS APPROVED BY THE PCBU OF THE PROJECT

Under the Work Health and Safety Regulation (WHS Regulation), a person conducting a business or undertaking (PCBU) is required to ensure that a safe work method statement (SWMS) is prepared before the proposed work starts.

Full Name:		
Signature:	Title:	Date:
Details of the person(s) responsible for ensuring implementation, monitoring compliance of the SWMS as well as reviews and modifications of the SWMS.		
Full Name:	Title:	Phone:

### ALL PERSONNEL PARTICIPATING IN ANY ACTIVITY ON THIS SWMS MUST HAVE THE FOLLOWING COMMUNICATED

Safety meetings or toolbox talks will be scheduled in accordance with legislative requirements to first identify any site hazards, then to communicate those hazards and then to further take steps to either eliminate or control each hazard.

If an incident or a near miss occurs, all work must stop immediately. Depending on the severity of the incident, a meeting will be called with all workers to amend the SWMS if required. The meeting may also be an educational opportunity.

Any changes made to the SWMS after an incident or a near miss must be approved by the Person Conducting Business or Undertaking and communicated to all relevant personnel.

The SWMS must be kept and be available for inspection at least until the work is completed. Where a SWMS is revised, all versions should be kept. If a notifiable incident occurs in relation to which the SWMS relates, then the SWMS must be kept for at least two years from the occurrence of the notifiable incident.

### NAME OF ALL RELEVANT PERSONNEL WHO HAVE BEEN CONSULTED AND COMMUNICATED TO IN THE DEVELOPMENT AND APPROVAL OF THIS SWMS


### CLIENT OR PRINCIPAL CONTRACTOR DETAILS

Client:	SCOPE OF WORKS
Project Name:	
Project Address:	
Project Manager:	
Contact Phone:	
Date SWMS supplied to Project Manager:	







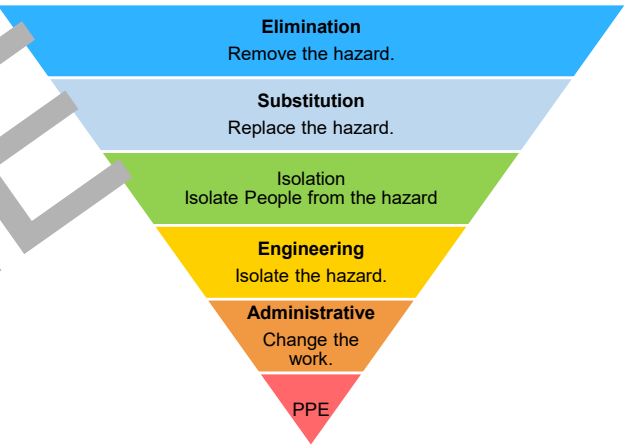





### ANY HIGH-RISK CONSTRUCTION WORK BEING CARRIED OUT

- |  |  |
|--|--|
| <input type="checkbox"/> involves a risk of a person falling more than 2 meters  | <input type="checkbox"/> is carried out on or near pressurised gas mains or piping                                     |
| <input type="checkbox"/> is carried out on a telecommunication tower   | <input type="checkbox"/> is carried out on or near chemical, fuel or refrigerant lines                                 |
| <input type="checkbox"/> involves demolition of an element of a structure that is load-bearing                           | <input type="checkbox"/> is carried out on or near energised electrical installations or services                      |
| <input type="checkbox"/> involves demolition of an element related to the physical integrity of a structure              | <input type="checkbox"/> is carried out in an area that may have a contaminated or flammable atmosphere                |
| <input type="checkbox"/> involves, or is likely to involve, disturbing asbestos  | <input type="checkbox"/> involves tilt-up or precast concrete  |
| <input type="checkbox"/> involves structural alteration or repair that requires temporary support to prevent collapse    | <input type="checkbox"/> is carried out on, in or adjacent to a road, railway, shipping lane or other traffic corridor |
| <input type="checkbox"/> is carried out in or near a confined space  | <input type="checkbox"/> is carried out in an area of a workplace where there is any movement of powered mobile plant  |
| <input type="checkbox"/> is carried out in/near a shaft or trench deeper than 1.5m or tunnel involving use of explosives | <input type="checkbox"/> is carried out in areas with artificial extremes of temperature.                              |
| <input type="checkbox"/> is carried out in or near water or other liquid that involves a risk of drowning.               | <input type="checkbox"/> involves diving work.   |

### ANY HIGH-RISK MACHINERY OR EQUIPMENT NEARBY

RISK MATRIX									
LIKELIHOOD	INSIGNIFICANT	MINOR	MODERATE	MAJOR	CATASTROPHIC	SCORE	ACTION	HEIRARCHY OF CONTROLS	
ALMOST CERTAIN	3 HIGH	3 HIGH	4 ACUTE	4 ACUTE	4 ACUTE			 <p><b>Elimination</b> Remove the hazard.</p> <p><b>Substitution</b> Replace the hazard.</p> <p><b>Isolation</b> Isolate People from the hazard</p> <p><b>Engineering</b> Isolate the hazard.</p> <p><b>Administrative</b> Change the work.</p> <p><b>PPE</b></p>	
LIKELY	2 MODERATE	3 HIGH	3 HIGH	4 ACUTE	4 ACUTE	4A ACUTE	DO NOT PROCEED		
POSSIBLE	1 LOW	2 MODERATE	3 HIGH	4 ACUTE	4 ACUTE	3H HIGH	Review before work starts.		
UNLIKELY	1 LOW	1 LOW	2 MODERATE	3 HIGH	4 ACUTE	2M MODERATE	Ensure control measures in place.		
RARE	1 LOW	1 LOW	2 MODERATE	3 HIGH	3 HIGH	1L LOW	Monitor and keep records		

**Notes on Hierarchy of Controls:** Elimination methods are the most effective and preferred when controlling a hazard. Substitution is the second most effective method of controlling a hazard. Engineering by isolation is the third most effective, while Administrative Controls by changing the work is the fourth most effective method. PPE (Personal Protective Equipment) is the least effective method.

PERSONAL PROTECTIVE EQUIPMENT (PPE)											
Select the appropriate PPE above suitable for the equipment used or the job task being performed (if applicable).											
FOOT PROTECTION	HAND PROTECTION	HEAD PROTECTION	HEARING PROTECTION	EYE PROTECTION	RESPIRATORY PROTECTION	FACE PROTECTION	HIGH-VIS CLOTHING	PROTECTIVE CLOTHING	FALL PROTECTION	SUN PROTECTION	HAIR/JEWELLERY SECURED
											
<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
Other PPE Required:											
Permit or Licenses Requirements						Mandatory Qualifications and Training					

JOB STEP	POTENTIAL HAZARDS	IR	CONTROL MEASURES	RR
SPECIFIC WORK STEPS	HAZARDS THAT MAY ARISE	INITIAL RISK	SPECIFIC MEASURES TO BE PUT IN PLACE TO ELIMINATE OR CONTROL THE RISKS	RESIDUAL RISK
Pre-start planning and consultation	<ul style="list-style-type: none"> <li>Inadequate scaffold design</li> <li>Unclear roles and responsibilities</li> <li>Unidentified underground services</li> <li>Traffic interaction with work area</li> <li>Inadequate emergency planning</li> </ul>	4A	<ul style="list-style-type: none"> <li>Review project scope and drawings and confirm that fixed scaffolding design, height, loading and access arrangements are suitable for the intended risks and duration</li> <li>Consult with the principal contractor and workers to identify site-specific hazards including overhead power lines, underground services, restricted access and adjacent public areas</li> <li>Verify whether a competent person or engineer certification is required under WHS Regulations and engage a suitably qualified person where scaffold will exceed 4 m in height or carry heavy or concentrated loads</li> <li>Prepare a task-specific Safe Work Method Statement (SWMS) for high risk construction work and ensure all workers read, understand and sign onto the document before starting work</li> <li>Define roles for riggers, doggers, spotters and supervisors and confirm each person holds the required PPL and competency for the type and height of scaffold to be erected</li> <li>Establish emergency response procedures for falls, structural collapse and electrical contact and brief all personnel on rescue methods, contact numbers and access points</li> <li>Schedule work to avoid extreme weather conditions where possible and plan contingency for stopping work during high winds, lightning or heavy rain</li> <li>Confirm exclusion of the public from the scaffold area and coordinate with site management regarding signed access ways and delivery times</li> </ul>	2M
Site inspection and preparation	<ul style="list-style-type: none"> <li>Uneven ground conditions</li> <li>Subsurface voids or services</li> <li>Unplanned vehicle movement</li> <li>Poor housekeeping</li> <li>Inadequate lighting</li> </ul>	3H	<ul style="list-style-type: none"> <li>Inspect the full scaffold footprint and surrounding area to identify soft ground, voids, pits, trenches, service covers and drainage lines that may affect scaffold stability</li> <li>Confirm location of underground services using current Dial Before You Dig information, site plans and, where necessary, non-destructive testing before driving any stakes or anchors</li> <li>Level and compact the ground under base plates and sole boards and eliminate trip hazards by removing rubble, offcuts and loose materials from the work area</li> <li>Install edge protection, barriers and signage to separate scaffold operations from site traffic routes, public access and plant operating zones</li> <li>Provide adequate task lighting for early morning, late afternoon or night operations and ensure temporary lighting is positioned to avoid glare or trip hazards</li> <li>Mark and maintain clear access paths for manual handling of components, avoiding steep slopes and slippery or muddy areas</li> <li>DO NOT commence scaffold erection on ground that is waterlogged, undermined, eroding or unable to support the design loads without engineer review and rectification</li> </ul>	1L
Establish exclusion zones and services checks	<ul style="list-style-type: none"> <li>Falling objects onto persons below</li> <li>Contact with live electrical services</li> </ul>	4A	<ul style="list-style-type: none"> <li>Install solid barricades or highly visible bunting with warning signage around the full scaffold erection and dismantling zone to prevent entry by non-essential persons</li> </ul>	2M

JOB STEP	POTENTIAL HAZARDS	IR	CONTROL MEASURES	RR
SPECIFIC WORK STEPS	HAZARDS THAT MAY ARISE	INITIAL RISK	SPECIFIC MEASURES TO BE PUT IN PLACE TO ELIMINATE OR CONTROL THE RISKS	RESIDUAL RISK
	<ul style="list-style-type: none"> <li>Unauthorised entry to work area</li> <li>Scaffold tilting from ground failure</li> </ul>		<ul style="list-style-type: none"> <li>Appoint a dedicated spotter to control access into the exclusion zone during crane lifts, component stacking and dismantling activities</li> <li>Identify all overhead electrical lines, building feed and temporary power leads near the planned scaffold and measure clearances in accordance with standard electrical safety requirements</li> <li>Consult the relevant electricity supply authority or a competent person to determine minimum approach distances and whether power isolation, de-energisation or physical barriers are required</li> <li>Position scaffolding so that metal components and workers cannot encroach the specified approach distance to live services; if this cannot be achieved DO NOT erect until power risk is eliminated or controlled</li> <li>Confirm ground bearing capacity using engineer advice where scaffolding will be multi-bay, multi-level or carrying heavy plant or materials to prevent scaffold tilting and foundation punch-through</li> <li>Display signage at all entry points stating 'Authorised Scaffolding Personnel Only' and 'Danger – Overhead Work in Progress'</li> </ul>	
Delivery and stacking of scaffold components	<ul style="list-style-type: none"> <li>Struck by moving plant</li> <li>Manual handling strain</li> <li>Unstable stacked components</li> <li>Pinch and crush points</li> </ul>	3H	<p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p>	2M
Base setup and prevention of scaffold tilting	<ul style="list-style-type: none"> <li>Scaffold base subsidence</li> <li>Incorrect sole board installation</li> <li>Overloading of ground supports</li> <li>Uncontrolled scaffold movement</li> </ul>	4A	<p>[REDACTED]</p>	2M

Partial erection  
al scaffold

JOB STEP	POTENTIAL HAZARDS	IR	CONTROL MEASURES	RR
SPECIFIC WORK STEPS	HAZARDS THAT MAY ARISE	INITIAL RISK	SPECIFIC MEASURES TO BE PUT IN PLACE TO ELIMINATE OR CONTROL THE RISKS	RESIDUAL RISK
Working at height during erection	<ul style="list-style-type: none"> <li>Falls from scaffold</li> <li>Leaning out from scaffolds</li> <li>Walking on incomplete decks</li> <li>Climbing on scaffolding</li> </ul>	4A	<p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p>	2M
Decking, planking and toe board installation	<ul style="list-style-type: none"> <li>Plank failure or displacement</li> <li>Gaps between platforms</li> <li>Falling tools and materials</li> <li>Foot entrapment on walking surfaces</li> </ul>	4A	<p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p> <p>[REDACTED]</p>	2M

JOB STEP	POTENTIAL HAZARDS	IR	CONTROL MEASURES	RR
SPECIFIC WORK STEPS	HAZARDS THAT MAY ARISE	INITIAL RISK	SPECIFIC MEASURES TO BE PUT IN PLACE TO ELIMINATE OR CONTROL THE RISKS	RESIDUAL RISK
Guardrails, access and temporary platforms	<ul style="list-style-type: none"> <li>Falls at access points</li> <li>Unprotected leading edges</li> <li>Unsafe temporary platforms</li> <li>Misuse of ladders</li> </ul>	4A		2M
Complex and high scaffolding configurations	<ul style="list-style-type: none"> <li>Design error in complicated setup</li> <li>Scaffold collapse</li> <li>Incorrect lean-to scaffold use</li> <li>Inadequate bracing of transom scaffoldings</li> </ul>	4A		2M



JOB STEP	POTENTIAL HAZARDS	IR	CONTROL MEASURES	RR
SPECIFIC WORK STEPS	HAZARDS THAT MAY ARISE	INITIAL RISK	SPECIFIC MEASURES TO BE PUT IN PLACE TO ELIMINATE OR CONTROL THE RISKS	RESIDUAL RISK
Use of scaffolding for elevated work	<ul style="list-style-type: none"> <li>• Overloading of platforms</li> <li>• Unsecured materials and equipment</li> <li>• Impact from moving tools</li> <li>• Improper use of scaffold stairways</li> </ul>	3H		1L
Inspection, maintenance and repair	<ul style="list-style-type: none"> <li>• Use of damaged scaffolding</li> <li>• Corrosion or cracked welds</li> <li>• Loose ties and fittings</li> <li>• Unrecorded modifications</li> </ul>	3H		1L

protection  
height  
road limits

3H

A large, light blue rectangular area with a diagonal line and a large, light blue 'SAMPLE' watermark. The watermark is oriented diagonally from the bottom-left to the top-right. The background is a solid light blue color.

## EMERGENCY RESPONSE – CALL 000 FOR EMERGENCIES

Ensure to have an Emergency Management Plan in place as well as adequate numbers of trained first aid staff with easy access to fully stocked first aid kits, rescue equipment, material safety data sheets, adequate access to emergency communication equipment and fire-fighting equipment suitable for all classes of fire and ignition sources.

## LEGISLATIVE REFERENCES

RELEVANT LEGISLATION AND CODES OF PRACTICE. DELETE THE LEGISLATIVE REFERENCES IF ANY STATE IS NOT APPLICABLE

### Queensland & Australian Capital Territory

Work Health and Safety Act 2011

Work Health and Safety Regulations 2011

Legislation QLD: <https://www.worksafe.qld.gov.au/laws-and-compliance/work-health-and-safety-laws>

Codes of Practice QLD: <https://www.worksafe.qld.gov.au/laws-and-compliance/codes-of-practice>

Legislation ACT: <https://www.worksafe.act.gov.au/laws-and-compliance/acts-and-regulations>

Codes of Practice ACT: <https://www.worksafe.act.gov.au/laws-and-compliance/codes-of-practice>

### Victoria

Occupational Health and Safety Act 2004

Occupational Health and Safety Regulations 2017

Legislation VIC: <https://www.worksafe.vic.gov.au/occupational-health-and-safety-act-and-regulations>

Codes of Practice VIC: <https://www.worksafe.vic.gov.au/compliance-codes-and-codes-practice>

### New South Wales

Work Health and Safety Act 2011

Work Health and Safety Regulations 2025

Legislation NSW: <https://www.safework.nsw.gov.au/legal-obligations/legislation>

Codes of Practice NSW: <https://www.safework.nsw.gov.au/resource-library/list-codes-of-practice>

### Western Australia

Work Health and Safety Act 2020

Work Health and Safety Regulations 2022

Legislation Western Australia: <https://www.commerce.wa.gov.au/worksafe/legislation>

Codes of Practice WA: <https://www.commerce.wa.gov.au/worksafe/codes-practice>

### Northern Territory

Work Health and Safety (National Uniform Legislation) Act 2011

Work Health and Safety (National Uniform Legislation) Regulation 2011

Legislation NT: <https://worksafe.nt.gov.au/laws-and-compliance/workplace-safety-laws>

Codes of Practice NT: <https://worksafe.nt.gov.au/laws-and-compliance/codes-of-practice>

### Safe Work Australia Links

Law and Regulation (All States): <https://www.safeworkaustralia.gov.au/law-and-regulation>

Model Codes of Practice: <https://www.safeworkaustralia.gov.au/resources-publications/model-codes-of-practice>

### Model Codes of Practice

- Managing noise and preventing hearing loss at work
- Confined spaces
- Labelling of workplace hazardous chemicals
- Managing risks of hazardous chemicals in the workplace
- Welding processes
- First aid in the workplace
- Managing the risk of falls at workplaces
- Hazardous manual tasks
- Managing the risk of falls in housing construction
- Managing electrical risks in the workplace
- Demolition work
- Excavation work
- Work health and safety consultation, cooperation and coordination
- Managing the work environment and facilities
- How to manage work health and safety risks
- Managing risks of plant in the workplace
- Construction work

### South Australia

Work Health and Safety Act 2012 (SA)

Work Health and Safety Regulations 2012 (SA)

Legislation for SA: <https://www.safework.sa.gov.au/resources/legislation>

Codes of Practice for SA: <https://www.safework.sa.gov.au/workplaces/codes-of-practice#COPs>

### Tasmania

Work Health and Safety Act 2012

Work Health and Safety (Transitional and Consequential Provisions) Act 2012

Work Health and Safety Regulations 2012

Work Health and Safety (Transitional) Regulations 2012

Legislation for TAS: <https://worksafe.tas.gov.au/topics/laws-and-compliance/acts-and-regulations>

Codes of Practice for TAS: <https://worksafe.tas.gov.au/topics/laws-and-compliance/codes-of-practice>

Details of permits, licenses or access required by regulatory bodies (add or delete as required):

- Permits from local council
- Authorisation to commence work
- Any required documents.

## SIGNATORIES OF THE SAFE WORK METHOD STATEMENT

The signed and dated personnel listed below have cooperated in the consultation and development of this Safe Work Method Statement which has been approved by the Person/s Conducting a Business or Undertaking (PCBU). In signing this Safe Work Method Statement each individual acknowledges and confirms that they have read this SWMS in full, having raised any questions for items on this Safe Work Method Statement that require clarification, and confirms that they are competent, skilled and knowledgeable for the task assigned to them. Every person acknowledges that they have received the relevant training and qualifications where required, before carrying out any work contained in this Safe Work Method Statement. By signing this Safe Work Method Statement each individual agrees to work safely, to follow any safe work instructions which are provided, and agrees to use all Personal Protective Equipment where appropriate.

Worker Name	Signature	Date

## SAFE WORK METHOD STATEMENT MONITORING AND REVIEW

**The SWMS must be reviewed regularly** to make sure it remains effective and must be reviewed (and revised if necessary) if relevant control measures are revised. The review must be carried out in consultation with workers (including contractors and sub-contractors) who may be affected by the operation of the SWMS and their health and safety representatives who represent that work group at the workplace.

When the SWMS has been revised the PCBU must ensure that all persons involved with the work are advised that a revision has been made and how they can access the revised SWMS, including all persons who will need to change a work procedure or system as a result of the review are advised of the changes in a way that will enable them to implement their duties consistently with the revised SWMS. All workers that will be involved in the work must be provided with the relevant information and instruction that will assist them to understand and implement the revised SWMS.

**The SWMS must be monitored regularly** for the effectiveness of ensuring hazard controls are effective in reducing the risk of incidents, keeping the workplace safe for all personnel. The person responsible for monitoring the effectiveness of the Safe Work Method Statement should employ a multi-faceted approach which includes but is not limited to:

1. Spot Checks.
2. Consultation with workers, contractors and sub-contractors.
3. Internal audits on a continual basis.

An approach of continuous improvement, promptly recording inconsistencies or deficiencies, followed up by immediate corrective action and consultation with all relevant personnel ensures that the PCBU is consistently developing ever-improving systems of safe work principles.

REVIEW NUMBER	1	2	3	4	5	6	7
NAME							
INITIALS							
DATE							

### SAFE WORK METHOD STATEMENT REVIEW CHECKLIST

This Safe Work Method Statement Review Checklist is to be followed and used upon initial development of the SWMS to help ensure that all steps have been adequately taken before work commences. Think of this document as an internal audit review checklist before commencing work, and may form part of a Toolbox Talk (safety meeting) and may be used as an opportunity for education and training.

ITEMS WHICH MUST BE INCLUDED IN THE SWMS	COMPLETED	COMMENTS
The company details have been entered, including the project name and address.	<input checked="" type="checkbox"/>	
All relevant personnel consulted during the development of the SWMS.	<input checked="" type="checkbox"/>	
Name, signature, position and date signed of the person approving the SWMS.	<input type="checkbox"/>	
Specific personnel and qualifications, experience is noted in the SWMS.	<input checked="" type="checkbox"/>	
Provides a step-by-step process of tasks required to carry out the activity or task.	<input checked="" type="checkbox"/>	
Adequate risk assessment of any identified hazards has been completed.	<input checked="" type="checkbox"/>	
Foreseeable hazards are identified and documented for each step.	<input checked="" type="checkbox"/>	
Any hazards listed in any site risk assessments have been added to the SWMS.	<input checked="" type="checkbox"/>	
SWMS initial risk (IR) column as well as residual risk (RR) column completed.	<input checked="" type="checkbox"/>	
Check control measures added to the SWMS are the most effective selected.	<input checked="" type="checkbox"/>	
Responsible person is assigned and listed on the SWMS for the implementation of control measures.	<input checked="" type="checkbox"/>	
Permit or licenses requirements specified, such as Hot Work, Electrical Work, Work at Heights etc.	<input checked="" type="checkbox"/>	
SWMS identifies plant and equipment to be used.	<input checked="" type="checkbox"/>	
Details of inspection checks required for any equipment listed and noted on the SWMS.	<input checked="" type="checkbox"/>	
Describes any mandatory qualifications, experience, training or skills required to perform the work.	<input checked="" type="checkbox"/>	
Applicable personal protective equipment is selected on the SWMS.	<input checked="" type="checkbox"/>	
Reflects and documents any legislative references and/or Australian Standards.	<input checked="" type="checkbox"/>	
Identifies any hazardous substances used with specific control measures in line with any SDS.	<input checked="" type="checkbox"/>	
<b>REVIEWED BY</b>		<b>DATE REVIEWED</b>
<b>SIGNATURE</b>		<b>DATE COMPLETED</b>
